




January 2026 PES Fiber Construction Update

We want to share a brief update on the progress of our fiber network expansion. The map below highlights different areas of construction and where things currently stand. Please see the status for your area below:

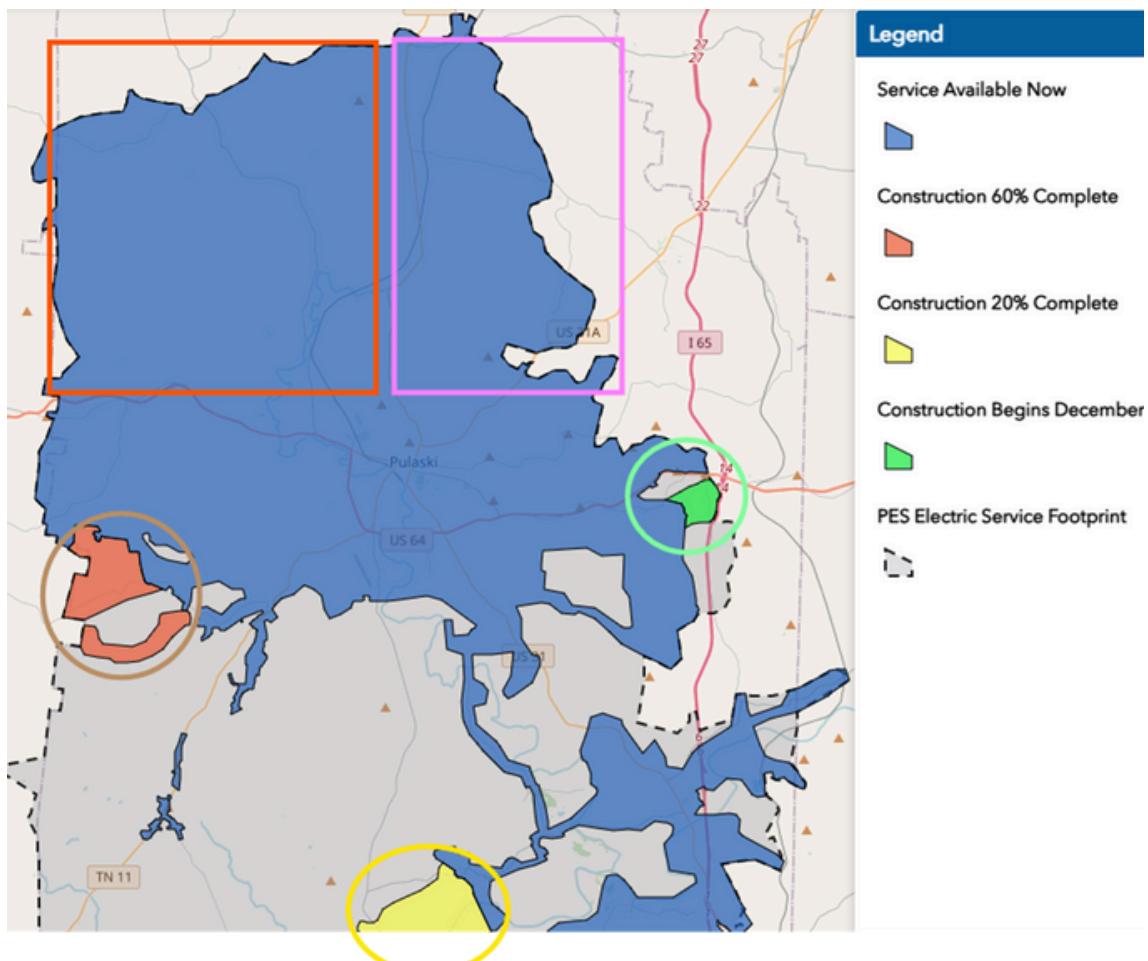

See page 2 for color-coded descriptions.



Red Area

We have 17 customers in this area who have recently signed up and require a service drop to be installed. A drop is the wire that runs from our network access point to the side of your home. Once these drops are constructed, installation appointments can be scheduled.

Purple Area

There are approximately 50 customers in this area who also require service drops to be constructed. After drop construction is completed, we will begin scheduling installations.

Brown Circle

Mainline fiber construction in this area is complete. Splicing work is approximately 80% complete and continues to move forward.

Green Circle

No construction has started yet in this area. Mainline construction is expected to be completed during the week of January 12.

Yellow Circle

Mainline construction is approximately 75% complete. Mainline work is also expected to be completed during the week of January 12.

We appreciate your patience as we work through each phase of construction. Our goal is to complete this work safely and efficiently so we can provide reliable service as soon as possible. Additional updates will be shared as progress continues.

Thank you for your continued support.

