



# November 10, 2025

## PES Fiber Expansion Update

Thanks for tuning in to another Fiber Expansion Update - we've got exciting news and progress to share!

### Phase 1 and 2



**Complete-Service is available.**

👉 New requests will be scheduled after the completion of Phase 3 installations.

### Phase 3 (9 Areas)



- **Drops Remaining:** 6 recently added (drop=fiber from the pole to the home.)
- **Installations Remaining:** 26 + 6 mentioned above. (Installation = fiber from the side of the home to the inside of the home).

### Phase 4 (5 Areas)

- **Drops Remaining:** 110 locations.
- **Next Step:** 31 + 110 mentioned above.

👉 Most of the remaining work in Phases 3 and 4 involves locations that requested service after the original contractor waitlist had closed.

### Phase 5 (4 Areas)

- **Pole Replacements:** 124 of 134 Complete
- **Construction:** Material arrived and construction is underway!

#### Project 1 - Fall River / Johnson Branch / Tin Top Road (See Map-Orange, north)

- **Mainline Fiber Construction:** **90% Complete**
- **Drop Construction:** **Underway**-Last days to get on the waitlist!
- **Goal:** Installations scheduled by **Dec. 1.**



## Project 2 – Charlie Howell Road (See map–Orange, South)


- **Mainline Construction: 60%** Complete
- **Drop Construction:** Begin in next 2 weeks. [Get on the waitlist now](#) to avoid delays
- **Goal:** Installations scheduled by **Dec. 15.**

## Project 3 – Turner Road (See Map–Yellow)

- **Mainline Fiber Construction: 20%** Complete
- **Drop Construction:** December
- **Target Construction Completion:** Dec. 31.
- **Goal:** Installations Begin: **January 2026.**

## Project 4 – Bunker Hill Road (See May–Green)

- **Mainline Fiber Construction:** Begins December
- **Drop Construction:** January
- **Target Construction Completion:** Jan. 9.
- **Goal:** Installations Begin: **February 2026**

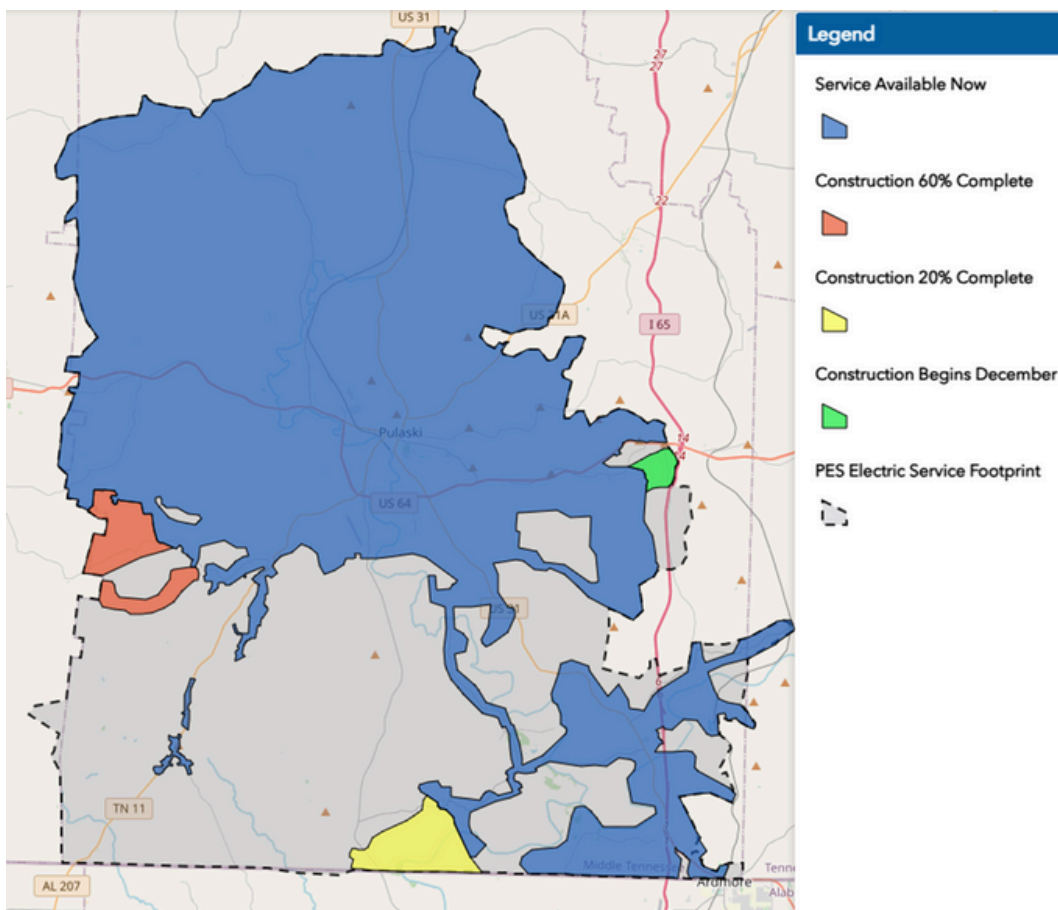

 The **PES website map** has been revised and now includes all of Phase 5. No further expansions are planned for 2025.

Final items on the close out inspection list are wrapping up this week in Phase 3 and 4.

## Exciting News

5 Gig is coming December 1!

Experience next-level speed—just schedule an installation appointment so we can upgrade your wiring for optimal performance.

**Thank You!**

---

